BROCKWELL PARK RESTORATION PROJECT - LANDSCAPING & BUILDING WORKS

BLAKEDOWN LANDSCAPES (SE) LTD - DRAFT CONSTRUCTION PROGRAMME - 14TH JULY 2011
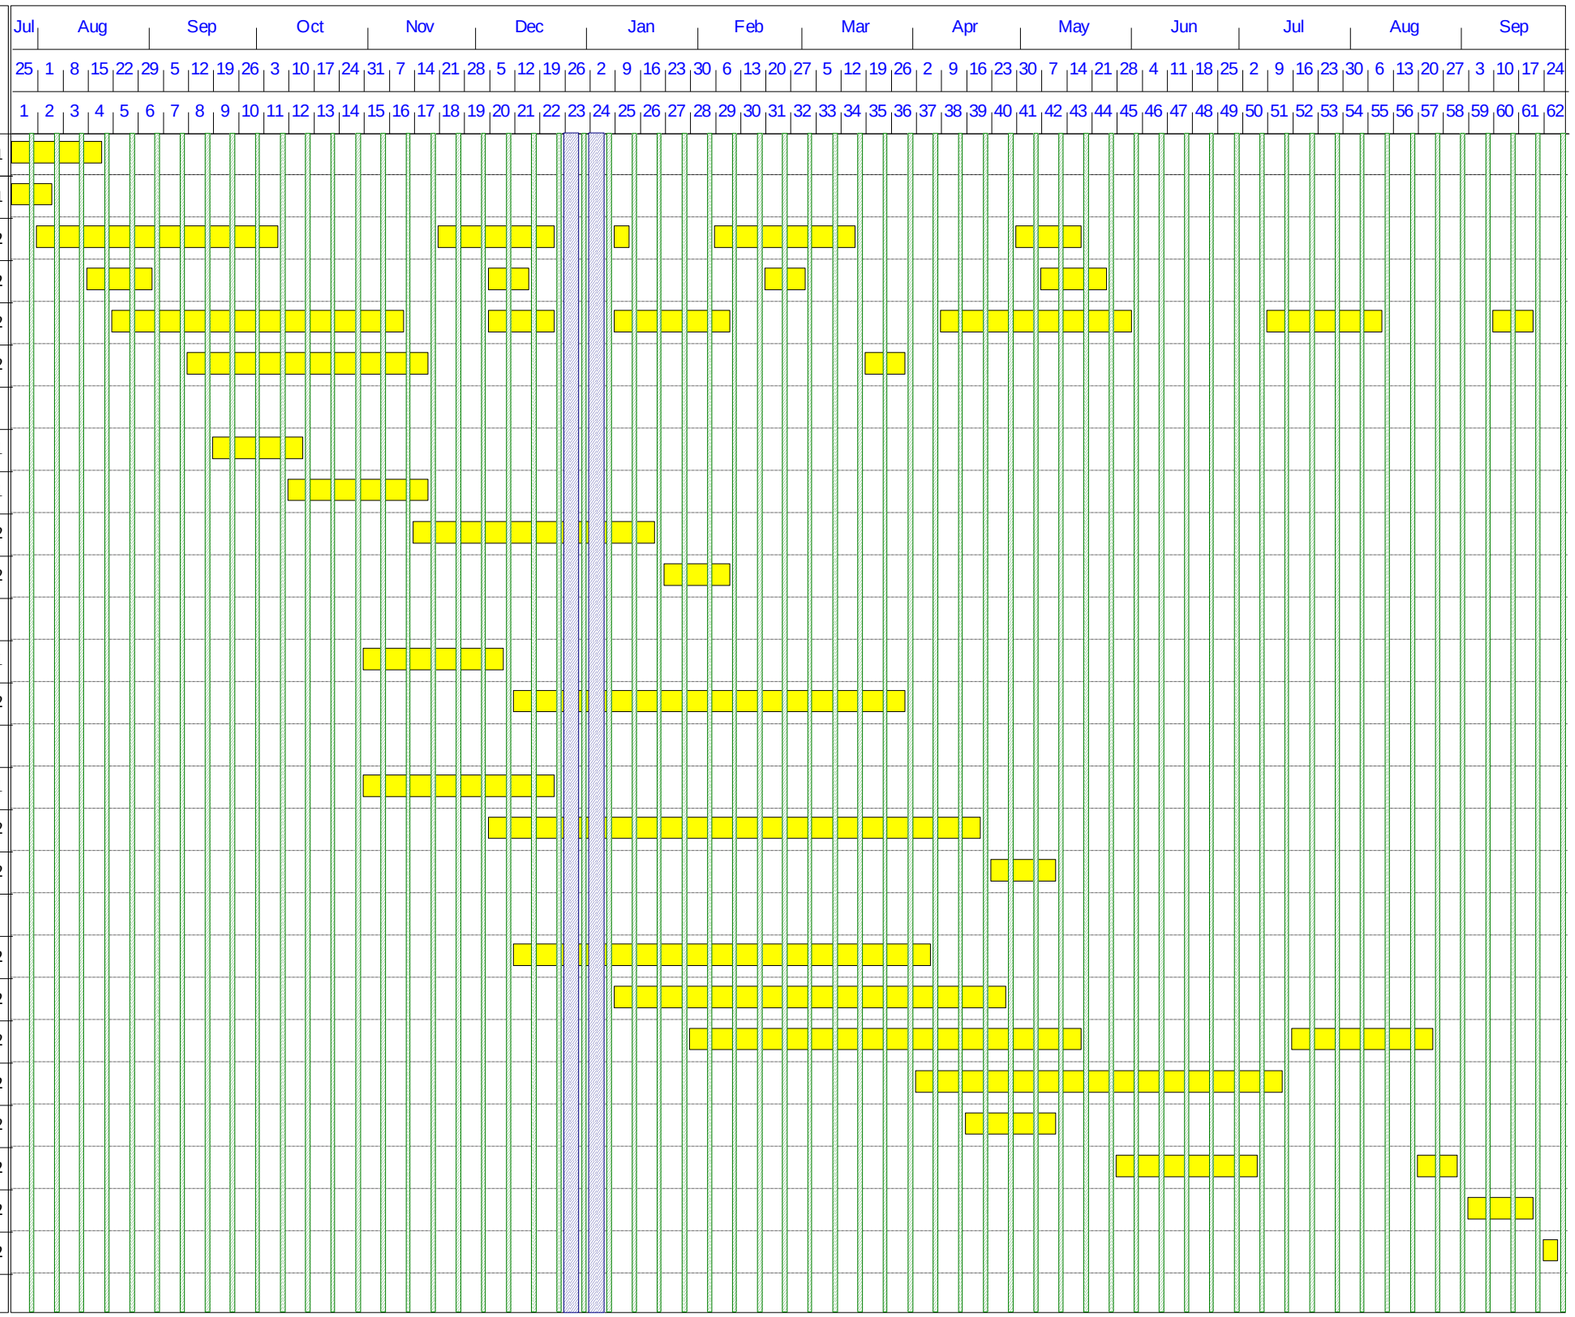
ID	Name	Start	Duration	Finish
1	**Design & Procurement**	25/07/11	20d	19/08/11
2	**Site Establishment**	25/07/11	10d	05/08/11
3	**Underground Drainage**	01/08/11	125d	18/05/12
4	**External Services**	15/08/11	50d	25/05/12
5	**Paths & Pavings Works**	22/08/11	175d	21/09/12
6	**Works to Walled Garden**	12/09/11	60d	30/03/12
7	**Works to Ponds**			
8	Site Clearance	19/09/11	20d	14/10/11
9	Drain and Desilt Ponds	10/10/11	30d	18/11/11
10	Pond Repairs/Construction	14/11/11	40d	20/01/12
11	Refill Ponds	23/01/12	15d	10/02/12
12	**Children's Playground**			
13	Demolitions	31/10/11	30d	09/12/11
14	New Playground	12/12/11	70d	30/03/12
15	**Soft Landscaping**			
16	Preparation of beds	31/10/11	40d	23/12/11
17	Planting	05/12/11	90d	20/04/12
18	Aquatic Marginal Planting	23/04/12	15d	11/05/12
19	**Building & Repair Works**			
20	Temple & Lodge	12/12/11	75d	06/04/12
21	Greenhouse Construction	09/01/12	80d	27/04/12
22	**Park Boundary Works**	30/01/12	110d	24/08/12
23	**Park Furniture/ Signage**	02/04/12	75d	13/07/12
24	**Works to Lido Area**	16/04/12	20d	11/05/12
25	**Park Entrance Works**	28/05/12	40d	31/08/12
26	**Clear Site/ Reinstatement**	03/09/12	15d	21/09/12
27	**Handover**	24/09/12	5d	28/09/12
28
